

Countywide Planning Monthly Project Updates


May 2021 Monthly Update

> Monthly Status of Major Projects

- West Santa Ana Branch
- Green Line to Torrance
- Eastside Transit Corridor Phase 2
- Sepulveda Transit Corridor
- NoHo to Pasadena BRT

> Countywide Planning Dashboard

ESFV + Pillar Projects Measure M Baseline Schedules

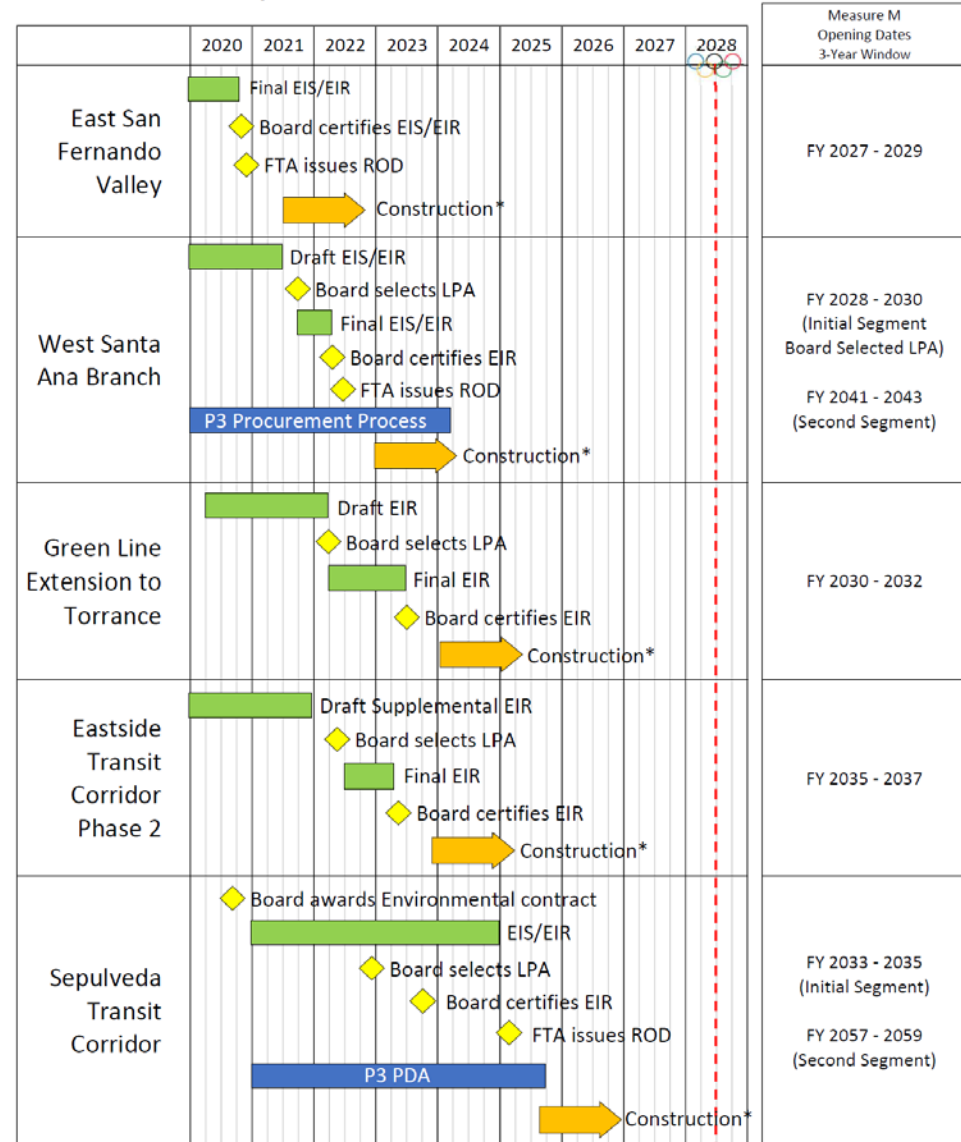

* Construction is inclusive of advanced utility relocation and right-of-way Schedules are subject to change based on funding and environmental review

West Santa Ana Branch Transit Corridor

> Status

- Draft EIS/EIR
 - Anticipated Draft Release: June/July 2021
 - Anticipated LPA Selection: Fall 2021

> Key Activities in April

- Incorporating 2nd round of FTA's comments on the Administrative Draft
- Report back on Funding Agreement Extension with the Gateway Cities COG
- Stakeholder Working Group meetings to provide project status update
- UPRR ongoing coordination on commercial development study
- 15% design work continues to conduct field surveys of utilities
- 3rd Party Coordination with Caltrans and Army Corps

> Next Actions

- Submit 3rd administrative draft to FTA
- Community engagement before release of Draft EIS/EIR



Green Line Extension to Torrance

> Status


- Draft EIR + Advanced Conceptual Engineering tasks are proceeding (15% design)

> Key Activities

- Review of over 700 comments received during the scoping period to incorporate necessary public issues into environmental review
- Ongoing coordination meetings with BNSF on shared track segments
- Engineering analysis of Hawthorne versus ROW technical issues

> Next Actions

- Ongoing outreach:
 - Cities, BNSF, Caltrans
 - Communities
- Summer Walking Tours with Community Stakeholders, Residents

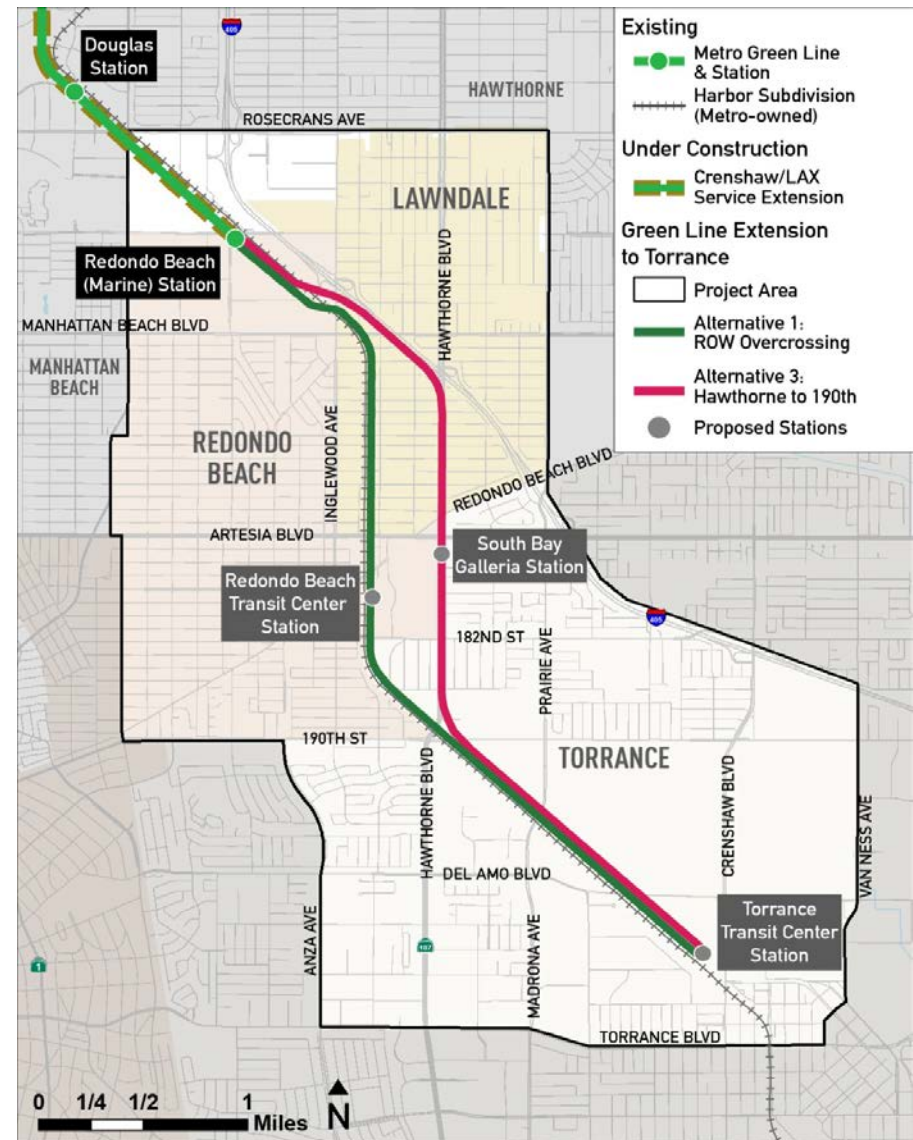


Eastside Transit Corridor Phase 2

> Status

- Environmental Analysis, Systems Engineering and Advanced Conceptual Engineering (ACE)

> Key Activities

- Community Based Organization (CBO) strategy continues to be developed in coordination with Community Relations and Race & Equity Departments:
 - CBO Strategy will serve as a platform to share local expertise, recommendations and methods
 - Meetings with key stakeholders
 - East LA Chamber of Commerce
 - Whittier Blvd Merchants
 - East LA Small Business Roundtable
 - Health Innovation Community partnership
 - Washington Coalition (April 1 and May 6)

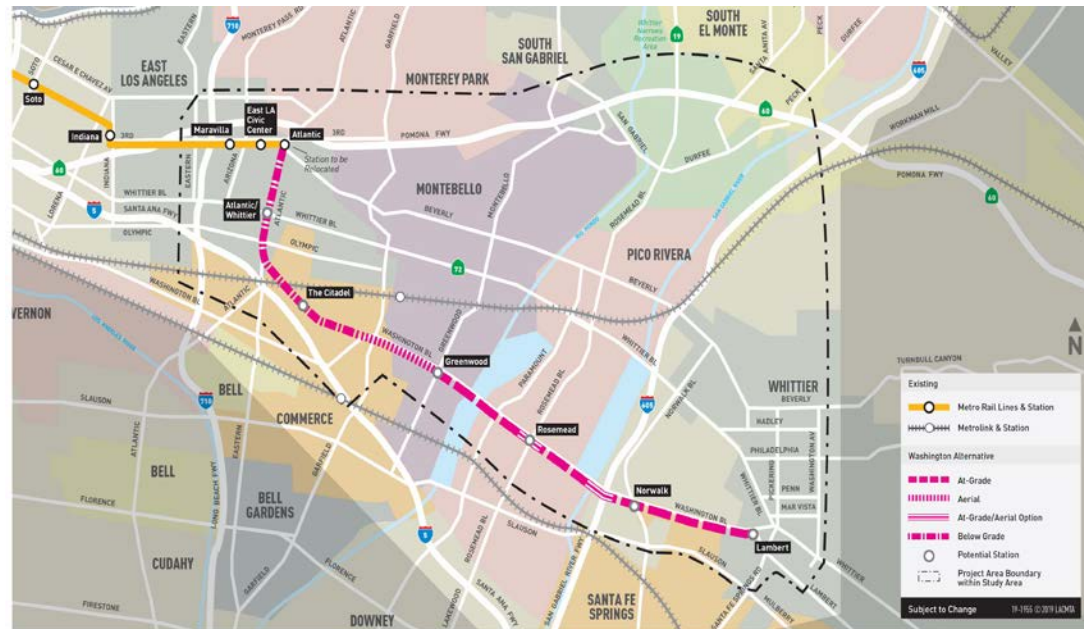

> Next Actions

- Continuing design and alternatives definition refinements of below ground segment, proposed Maintenance Yard sites and Washington Boulevard profile configurations in Montebello (aerial and at-grade)

Sepulveda Transit Corridor

> Status

- Five (5) alternatives advancing into environmental process:

1) Monorail Alternative

PDA proposal, All Aerial in 405 Freeway

2) Monorail Alternative

Similar to Alt 1 with underground connection to UCLA

3) Heavy Rail Alternative

PDA proposal Underground with an aerial section along Sepulveda Boulevard in the San Fernando Valley

4) Heavy Rail Alternative

All Underground, similar to Alt #3 including along Sepulveda Boulevard in the San Fernando Valley

5) Heavy Rail Alternative

All Underground, including along Van Nuys Boulevard in the Valley instead of Sepulveda Boulevard

> Key Activities

- Preparing Notice to Proceed (NTP) for PDA teams

> Next Actions

- Community Forum on environmental process and schedule to be held June 8, 2021.
- Preparation for Environmental Scoping Period in fall 2021



NoHo to Pasadena BRT

> Status

- Staff has developed a refined Proposed Project based on DEIR comments received and subsequent stakeholder feedback

> Key Activities

- Ongoing stakeholder outreach to inform Proposed Project
- Conducted 3 meetings with Eagle Rock stakeholders and businesses (80 total participants) in March 2021
- Corridor-wide community meeting held April 1, 2021 (369 total attendees) to present the recommended Proposed Project prior to Board approval in May
- In April, staff provided response to December Board motion on optional left-side boarding

> Next Actions

- Separate board report for approval of Proposed Project Preferred Alternatives



Countywide Planning Dashboard

Pillar Projects									
	Project Name	Env Completion (FY)	Measure M Opening (FY)	Project Phase				Date	Action/Status
				AA	Draft Env	Final Env	Construction		
1	West Santa Ana Branch LRT	2022	2028-2030		X			April 2021	Approve Gateway COG Funding Agreement Modification and Extension
								July 2021	Release of Draft EIS/EIR
2	Green Line Extension to Torrance LRT	2023	2030-2032		X			April 2021	Review of EIR Scoping comments
								March 2022	Receive Draft EIR and Select Locally Preferred Alternative
3	Eastside Transit Corridor Phase 2	2024	2035-2037		X			Fall 2021	Select Locally Preferred Alternative (LPA)
4	Sepulveda Transit Corridor	2025	2033-2035	X				Fall 2021	Environmental Scoping

Other Measure M Projects									
	Project Name	Env Completion (FY)	Measure M Opening (FY)	Project Phase				Date	Action/Status
				AA	Draft Env	Final Env	Construction		
5	East San Fernando Valley Transit Corridor LRT	2020	2027-2029				X	Summer 2021	Environmental Clearance completed; initiate Supplemental ROW Study.
6	North San Fernando Valley BRT	2021	2023-2025		X			Summer 2021	Approve Proposed Project
7	North Hollywood - Pasadena BRT	2022	2022-2024		X			May 2021	Receive Draft EIR Select Proposed Project and approve Title VI Service Equity Analysis
8	Crenshaw Northern Extension LRT	2023	2047-2049		X			April/May 2021	EIR Scoping Period
9	LA River Path (central gap)	2024	2025-2028		X			January 2022	Receive Draft EIR and Select Locally Preferred Alternative
10	Vermont Transit Corridor	2024	2028-2030	X				May 2021	Award Environmental Contract

Non-Measure M Projects				Project Phase					
	Project Name	Env Completion (FY)	Opening/ Completion (FY)	AA	Draft Env	Final Env	Construction	Date	Action/Status
11	Centinela Grade Separation	2021	2025			X		Summer 2021	Approve funding and project delivery plan
12	LAUS Forecourt and Esplanade Improvements	2021	2023			X		June 2022	Life of Project Approval
13	Rio Hondo Confluence Station Feasibility Study	TBD. Feasibility Study anticipated to be completed in 2022	TBD	X				TBD	Receive Feasibility Study Report and determine next steps for the potential Rio Hondo Confluence Station
14	Rail-to-River ATC (Segment B)	TBD. Supplemental study	TBD	X				Fall 2021	Receive Supplemental Alternatives Analysis Select Revised Locally Preferred Alternative
15	Arts District/ 6th Street Station HRT	TBD	TBD		X			April 2021	Initiate EIR Scoping
16	First/Last Mile Implementation in Transit Corridor Projects (PLE 2 and forward)	varies by project	varies by project					Summer 2021	Approve FLM Plan for PLE 1; Other periodic project-specific actions in the future;

Strategies/ Policies				Phase			
	Project Name	Groundbreaking / Initiation (FY)	Opening/ Completion (FY)	Policies/ Strategic Plans	Implementation Plans	Date	Action/Status
17	Transit Oriented Communities (TOC) Implementation Plan:Semi-Annual Reports	Ongoing	Ongoing		X	Summer 2021	Report on TOC Implementation Plan Semi Annual Reports
18	BRT Vision and Principles Study	2019	2021	X		June 2021	Response to March 2021 Board Motion
19	First/Last Mile Guidelines	N/A	N/A	X		May/June 2021	Adopt Guidelines
20	Joint Development Policy	N/A	N/A	X		May 2021	Joint Development Policy Paper published and presented at January Board Adopt Revisions to Policy
