
Countywide Planning Monthly Project Updates

April 2021 Monthly Update

- > Monthly Status of Major Projects
 - West Santa Ana Branch
 - Green Line to Torrance
 - Eastside 2 Extension
 - Sepulveda Transit Corridor
 - NoHo to Pasadena BRT
- > Countywide Planning Dashboard



ESFV + Pillar Projects Measure M Baseline Schedules

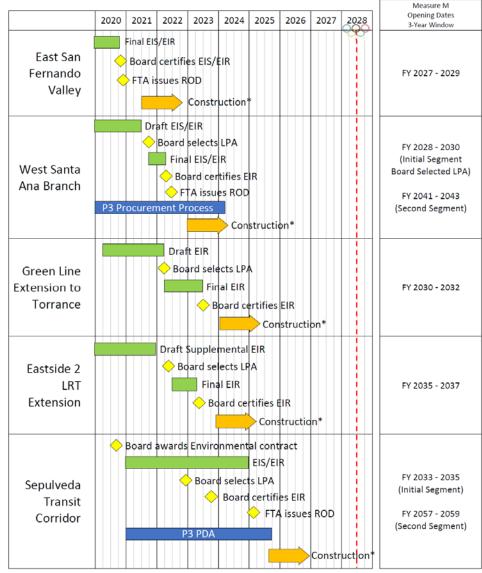

Construction is inclusive of advanced utility relocation and right-of-way
 Schedules are subject to change based on funding and environmental review

West Santa Ana Branch Transit Corridor


> Status

- Draft EIS/EIR
 - o Anticipated Draft Release: June/July 2021
 - o Anticipated LPA Selection: Fall 2021

> Key Activities

- March 2021- Submitted 2nd Administrative Draft to FTA
- April 2021- Board action to approve extension of existing Funding Agreement with the Gateway Cities COG for Third-Party Administration in the WSAB environmental clearance study

- Address second round of comments
- Community engagement before release of Draft EIS/EIR

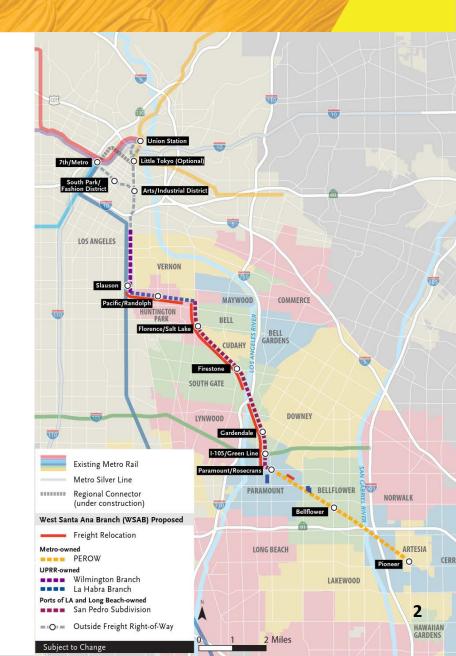

Green Line Extension to Torrance

> Status


 Draft EIR + Advanced Conceptual Engineering tasks are proceeding (15% design)

> Key Activities

- Environmental Scoping 45-day Comment Period concluded on March 29, 2021
 - Over 300 attendees
 - Over 700 comments received
- Review and incorporate necessary public issues into environmental review
- Ongoing coordination meetings with BNSF on shared track segments
- Engineering analysis of Hawthorne versus ROW technical issues

- Ongoing outreach:
 - Cities, BNSF, Caltrans
 - Communities



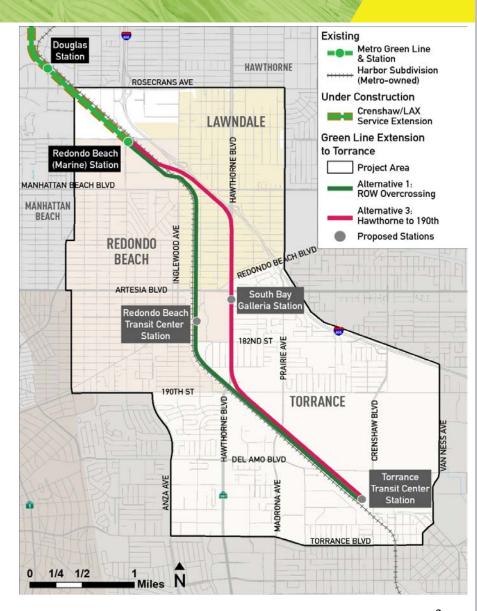


Eastside Transit Corridor Phase 2

> Status

 Environmental Analysis, Systems Engineering and Advanced Conceptual Engineering (ACE)

> Key Activities

- Developing Community Based Organization approach
 - Collaborative effort with Community Relations and Race and Equity Departments
 - Guidance from Equity Platform and the Draft CBO Partnering Strategy
 - CBOs Strategy will serve as a platform to share local expertise, recommendations and methods for implementing public awareness and engagement opportunities
- Orientation meetings with new Board Director Fernando Dutra and staff

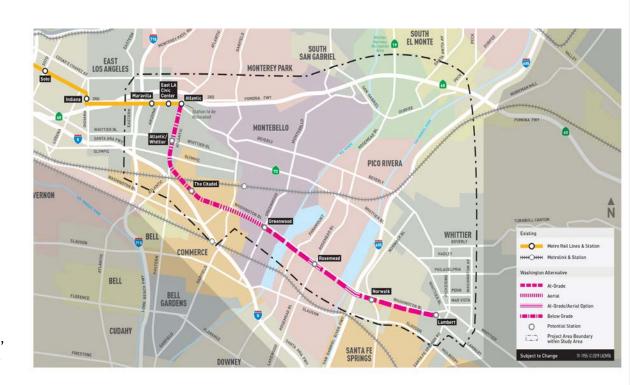

- April 1, 2021 Meeting with Washington Blvd Coalition
- Design refinements of below ground segment, proposed Maintenance Yard sites and Washington Boulevard profile configurations



Sepulveda Transit Corridor

> Status

- Two PDA contracts authorized at March 2021 Board Meeting:
 - LA SkyRail Express
 - Monorail technology in I-405 Right of Way
 - John Laing Investments and BYD Transit Solutions
 - Sepulveda Transit Corridor Partners
 - Heavy Rail Technology in subway/aerial configurations
 - Bechtel Development, Meridiam
 Sepulveda and American Triple I Partners

> Key Activities

Preparing Notice to Proceed (NTP) for both contractors

- Preparation for Environmental Scoping Meetings and Comment Period
- Community Outreach on environmental process and schedule





NoHo to Pasadena BRT

> Status

 Staff is developing a recommended Proposed Project based on DEIR comments received and subsequent stakeholder feedback

> Key Activities

 Ongoing stakeholder outreach to inform Proposed Project



- o 3 meetings with Eagle Rock stakeholders and businesses (80 total participants) in March 2021
- Corridor-wide community meeting scheduled for April 1, 2021 to present Proposed Project recommendation

- April 2021 Staff response to December Board motion on optional left-side boarding
- May 2021 Seek Metro Board approval of Proposed Project



Countywide Planning Dashboard

Pillar Projects										
					Project Phase					
_	Project Name	Env Completion (FY)	Measure M Opening (FY)	AA	Draft Env	Final Env	Construction	Date	Action/Status	
1	West Santa Ana Branch LRT	2022	2028-2030		х			April 2021	Approve Gateway COG Funding Agreement Modification and Extension	
								July 2021	Release of Draft EIS/EIR	
2	Green Line Extension to Torrance LRT	2023	2030-2032		Х			April 2021	Review of EIR Scoping comments	
2								March 2022	Receive Draft EIR and Select Locally Preferred Alternative	
3	Eastside Transit Corridor Phase 2	2024	2035-2037		X			Fall 2021	Select Locally Preferred Alternative (LPA)	
4	Sepulveda Transit Corridor	2025	2033-2035	Х				Fall 2021	Environmental Scoping	
Othe	Other Measure M Projects									
	Project Name	Env Completion (FY)	Measure M Opening (FY)	AA	Draft Env	Final Env	Construction	Date	Action/Status	
5	East San Fernando Valley Transit Corridor LRT	2020	2027-2029				х	Summer 2021	Environmental Clearance completed; initiate Supplemental ROW Study.	
6	North San Fernando Valley BRT	2021	2023-2025		Х			Summer 2021	Approve Proposed Project	
7	North Hollywood - Pasadena BRT	2021	2022-2024		Х			May 2021	Receive Draft EIR Select Proposed Project and approve Title VI Service Equity Analysis	
8	Crenshaw Northern Extension LRT	2023	2047-2049		Х			April/May 2021	EIR Scoping Period	
9	LA River Path (central gap)	2024	2025-2028		Х			January 2022	Receive Draft EIR and Select Locally Preferred Alternative	
10	Vermont Transit Corridor	2024	2028-2030	Х				May 2021	Award Environmental Contract 7	

Non-Measure M Projects										
					Project	: Phase				
	Project Name	Env Completion (FY)	Opening/ Completion (FY)	AA	Draft Env	Final Env	Construction	Date	Action/Status	
11	Centinela Grade Separation	2021	2025			X		Summer 2021	Approve funding and project delivery plan	
12	LAUS Forecourt and Esplanade Improvements	2021	2023			х		June 2022	Life of Project Approval	
13	Rio Hondo Confluence Station Feasibility Study	TBD. Feasibility Study anticipated to be completed in 2022	TBD	х				TBD	Receive Feasibility Study Report and determine next steps for the potential Rio Hondo Confluence Station	
14	Rail-to-River ATC (Segment B)	TBD. Supplemental study anticipated	TBD	Х				Fall 2021	Receive Supplemental Alternatives Analysis Select Revised Locally Preferred Alternative	
15	Arts Dristrict/ 6th Street Station HRT	TBD	TBD		Х			April 2021	Initiate EIR Scoping	
16	First/Last Mile Implementation in Transit Corridor Projects (PLE 2 and forward)	varies by project	varies by project					Summer 2021	Approve FLM Plan for PLE 1; Other periodic project- specific actions in the future;	
Strat	tegies/ Policies									
Julia	Strategiesy Polities				Phase					
	Project Name	Groundbreaking/ Initiation (FY)	Opening/ Completion (FY)	Policies/ Strategic Plans	Implementation Plans		Date	Action/Status		
17	Transit Oriented Communities (TOC) Implementation Plan:Semi-Annual Reports	Ongoing	Ongoing		х		Summer 2021	Report on TOC Implementation Plan Semi Annual Reports		
18	BRT Vision and Principles Study	2019	2021	Х			June 2021 Response to March 2021 Board Motion		March 2021 Board Motion	
19	First/Last Mile Guidelines	N/A	N/A	Х	x		May/June 2021	Adopt Guidelines		
20	Joint Development Policy	N/A	N/A	Х			May 2021	Joint Develop January Board Adopt Revisio		
