



Next Stop: clean air.


Cesar Chavez Bus Stop Improvement Project



Metro



Background

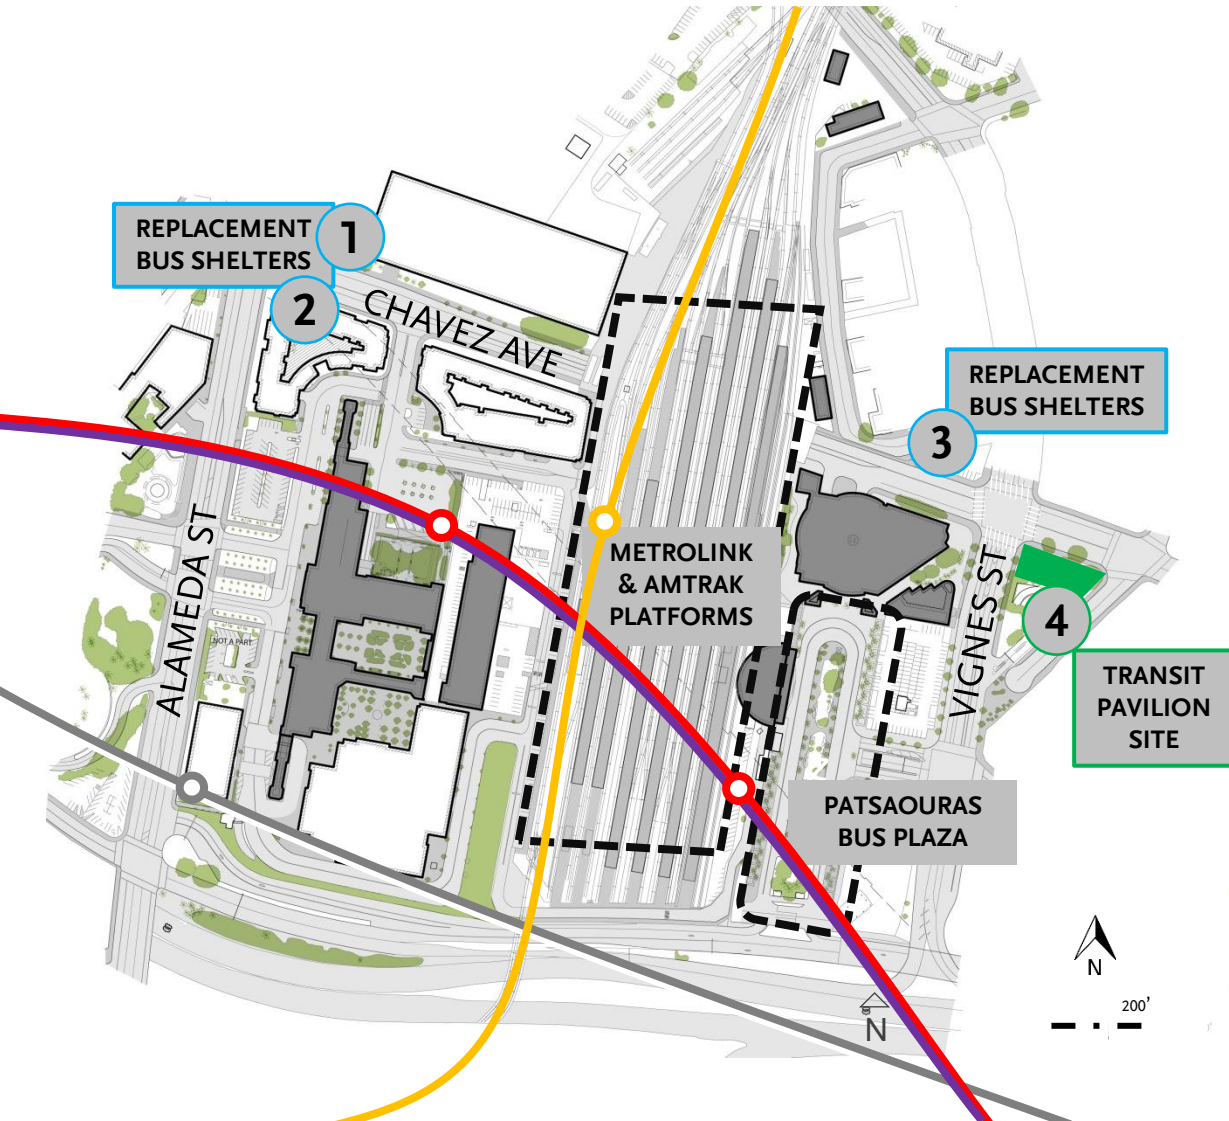

IMPROVEMENT SITES

- 1** METRO BUS LINES 33, 68, 70, 71, 78/79/378, 733
- 2** METRO BUS LINES 33, 40, 70, 71, 78/79/378, 84/68, 442, 733
- 3** METRO BUS LINES 40, 68, 70, 71, 78/79/378, 733
- 4** METRO BUS LINES 40, 70, 71, 78/79/378, 84/68, 442, 770

-  METRO GOLD LINE
-  METRO RED/PURPLE LINE
-  METRO SILVER LINE



Background



- 2014:
 - Metro Secured FTA Grant based on a project concept
 - Board approved LOP of \$2,085,697 (20% local match)
- 2015-2017:
 - Environmental cleared
 - Outreach conducted
 - Sustainability elements incorporated
- 2018:
 - Design completed
 - Construction solicitation
 - Construction bids received

Recommended Action



CONSIDER:

- A. AUTHORIZING an increase in the life of project (LOP) budget by \$1,430,000 for the Cesar Chavez Bus Stop Improvements Project from \$2,100,000 to \$3,530,000; and

- B. AMENDING the FY19 budget to increase Project 210041 funding by \$1,850,000.





Outreach



On-site outreach meetings targeted the users of the bus stops

- Meeting 1:
 - November 2016
 - Gathered input from patrons on priorities for the site
- Meeting 2:
 - February 2018
 - Shared the design of the site with patrons
 - Gathered input on station name

Outreach

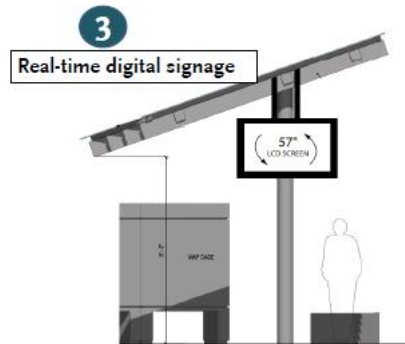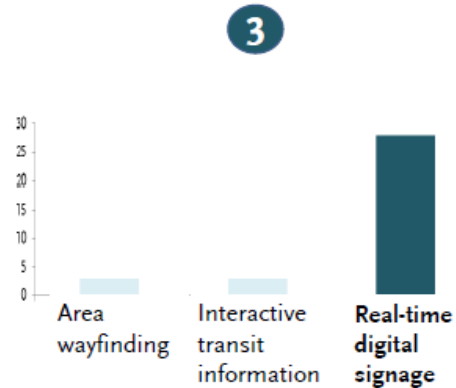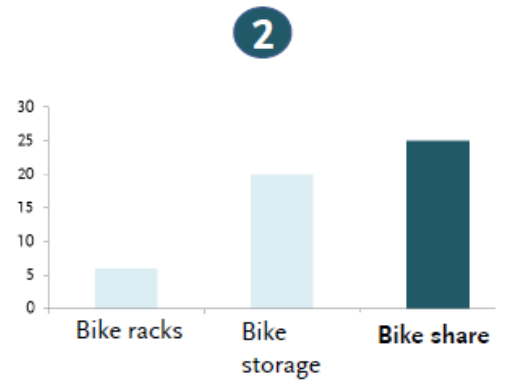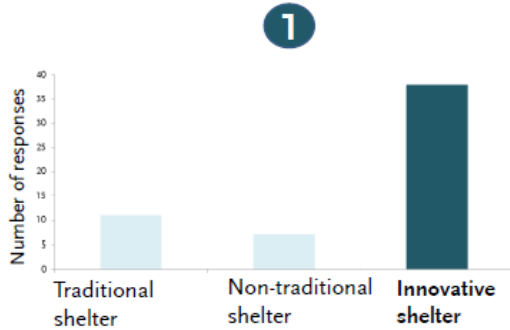




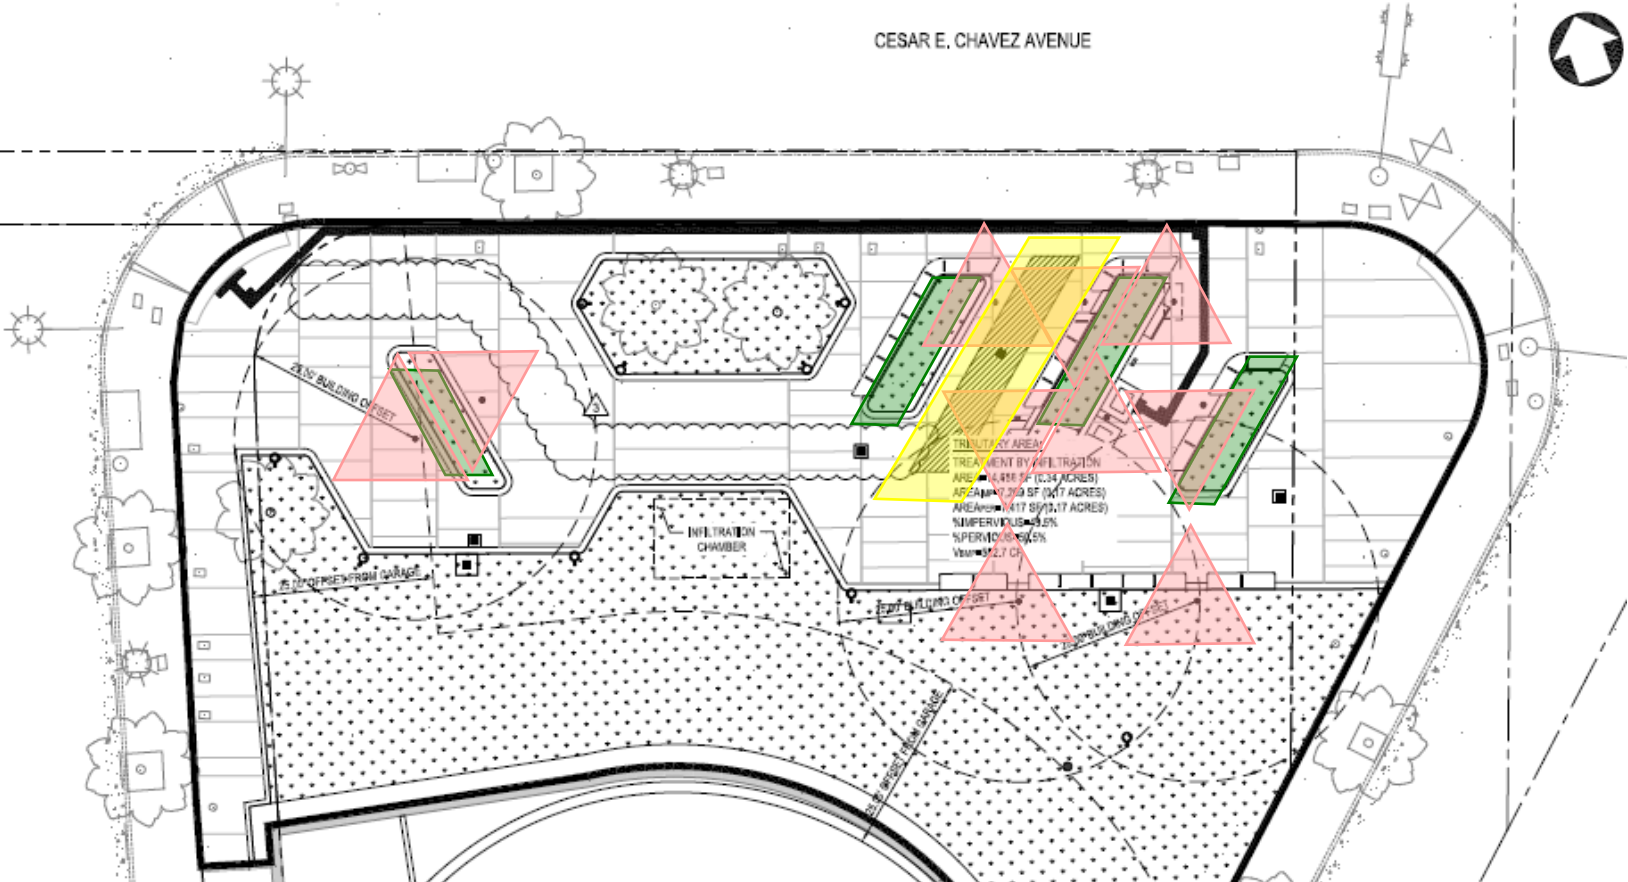
Proposed Design



Sustainability Features



-  Piezoelectric tiles
-  Solar panels
-  Rainwater catchment



Schedule / Next Steps



- Early 2019:
 - Award construction contract
 - Begin construction
- Late 2019:
 - Complete construction
- Early 2020:
 - Close out grant
