

# Measure M Independent Taxpayer Oversight Committee

## Transit Projects Update

Allison Yoh, Executive Officer  
March 6, 2024

# Measure M Transit Projects




## > Major Pillar Projects

- (1) Southeast Gateway Line
- (2) C Line Extension to Torrance
- (3) Sepulveda Transit Corridor
- (4) Eastside Transit Corridor Phase 2

## > Other Projects in Planning

- Vermont Transit Corridor
- K Line Northern Extension

# Southeast Gateway Line (formerly West Santa Ana Branch Transit Corridor)



Current Phase	Most Recent Cost Estimate
Final EIR/EIS	IOS - \$7.1B (YOES, forecast completion 2035)

## Recent Activities

- Nov 2023: Board authorized contract for advanced engineering and final design
- Dec 2023: 2<sup>nd</sup> Admin Draft of Final EIS/EIR submitted
- Jan 2024: Ports of Los Angeles/Long Beach authorized execution of MOU, completion of public voting tally and ceremony marking the new name
- Program Management Support Services (PMSS) procurement underway (blackout)


## Next Actions

- Working with FTA on submittal for entering next stage of project development
- Spring 2024 (tent.): Board certification of Final EIR (Project approved per CEQA), then FTA Record of Decision for EIS (Project approved per NEPA)





# Eastside Transit Corridor Phase 2



## Current Phase

EIR  
(NEPA TBD)

## Most Recent Cost Estimate

IOS - \$7.9B  
(2031\$, midpoint of construction)


- Oct-Dec: Community Rail Tours
  - Elected officials/public agencies
  - CBO/youth/key stakeholders
  - 2 public tours
- Jan: First/Last Mile Partnership Briefing (corridor partners and elected officials), virtual tour showcasing FLM projects with City of Long Beach
- Engaging CBOs in Community Walk audits for first/last mile study
- Reviewing comments received from corridor cities on draft Master Cooperative Agreement
- Admin Final EIR circulated for internal review



## Next Actions

- Complete CEQA document for release in early Spring 2024 followed by Board certification (Project approved per CEQA)
- Continue to coordinate with FTA on appropriate timing to initiate NEPA and entry into Project Development phase

# Sepulveda Transit Corridor




Current Phase	Most Recent Cost Estimate
EIR	\$5.7B (2015\$)

## Recent Activities

- Design refinements underway, reaching design freeze for environmental study
- Continued coordination w/ adjacent projects
- Ongoing geotechnical/seismic fieldwork
- Caltrans Project Report to be conducted following LPA selection


## Next Actions

- Continue to develop designs, environmental technical studies
- Draft EIR release anticipated early 2025

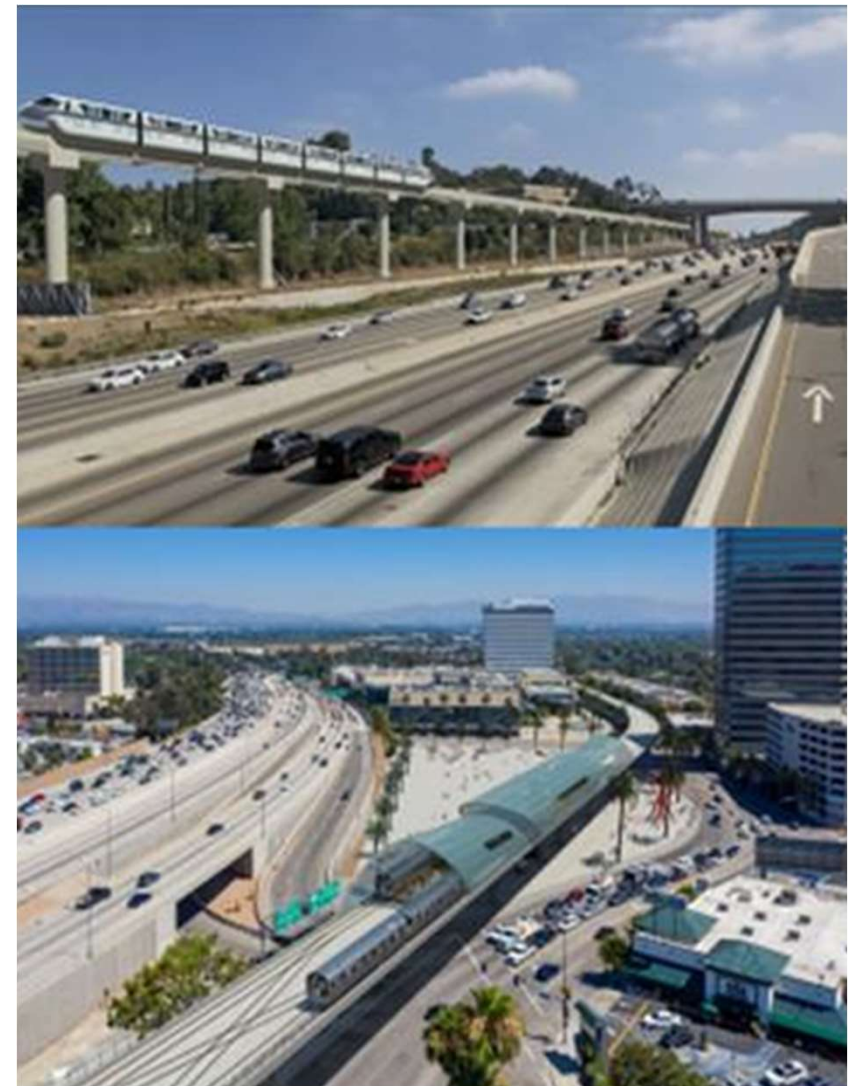



# C (Green) Line Extension to Torrance




Current Phase	Most Recent Cost Estimate
EIR	\$891M (2015\$)

## Recent Activities


- Provided support for outreach events hosted by Supervisor Mitchell (SD-2)
  - Community walking tour (December 2023)
  - Outreach meeting at affordable housing community (January 2024)
- South Bay Cities Council of Governments (COG) voted support for the Project, neutral on alignment (January 2024)

## Next Actions

- Prepare staff recommendation of Locally Preferred Alternative (LPA) based on project objectives, findings, community concerns
- Board selection of LPA

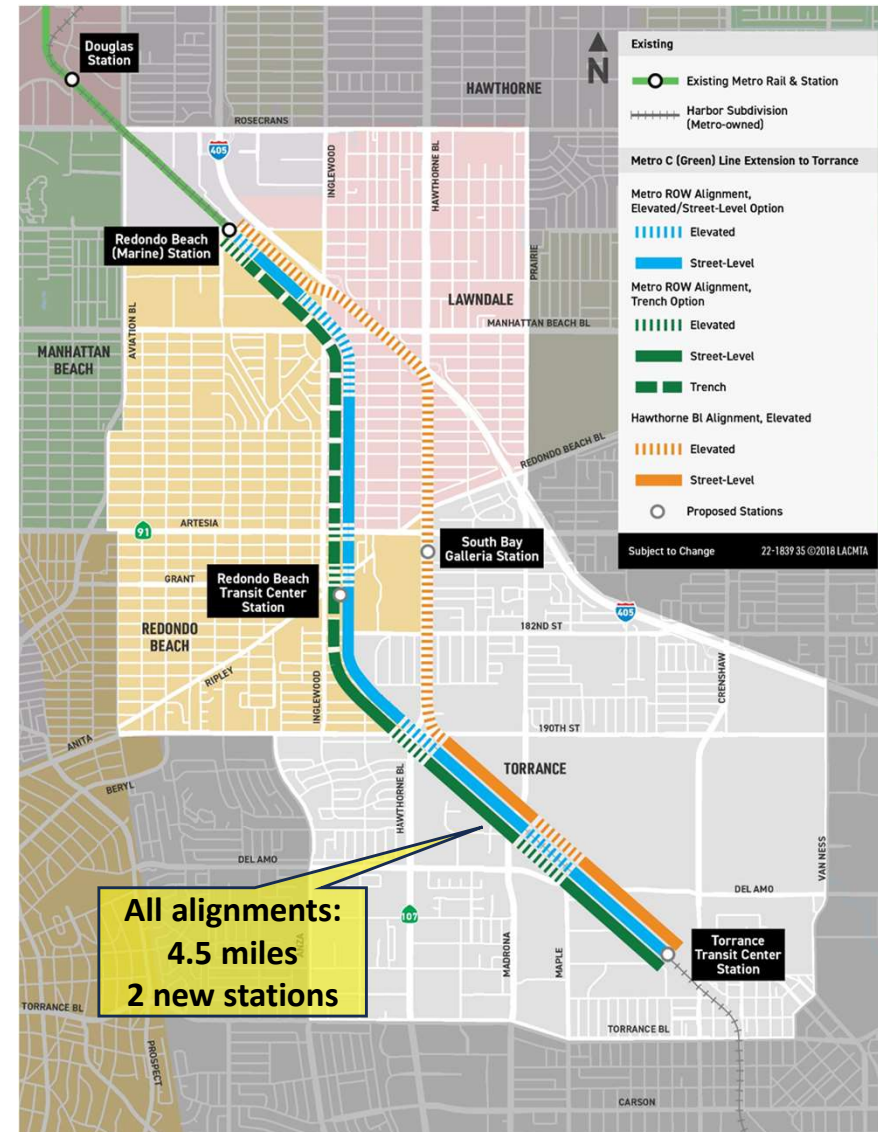

# Vermont Transit Corridor




Current Phase	Most Recent Cost Estimate
Preliminary Studies	\$425M (2015\$)

## Recent Activities

- Nov 2023: Initiated planning and environmental study for BRT; presentation to Early Intervention Team (EIT)
- Dec 2023: Issued Task Order for communications/ outreach services; community engagement for near, mid, and long-term improvements
- CBO Roundtable meetings are underway
- Formation of technical working group, work underway
- Meetings with neighborhood councils along the corridor


## Next Actions

- Continue planning and design for BRT, informed by CBO/outreach efforts
- Identify schedule for Notice of Preparation, Scoping

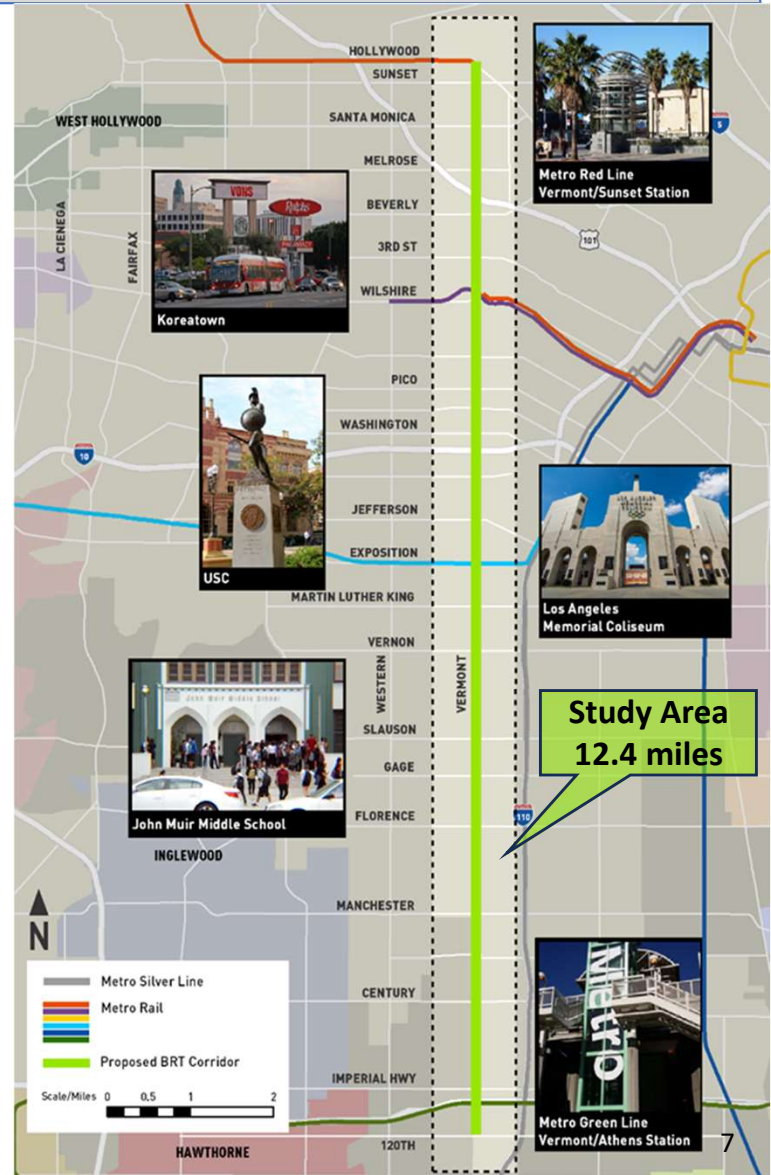



# K Line (Crenshaw) Northern Extension



Current Phase	Most Recent Cost Estimate
EIR	\$2.24B (2015\$)

## Recent Activities

- Finalizing tech reports for Draft EIR
- Advancing environmental analysis under CEQA
- Project newsletter recapping outreach activities in 2023
- Continue to identify cost and funding opportunities, phasing scenarios

## Next Actions

- Prepare chapters for Draft EIR
- Continue stakeholder engagement

