

Countywide Planning Monthly Project Updates

June 2021 Monthly Update


> Monthly Status of Major Projects

- West Santa Ana Branch
- Green Line to Torrance
- Eastside Transit Corridor Phase 2
- Sepulveda Transit Corridor
- NoHo to Pasadena BRT

> Countywide Planning Dashboard



ESFV + Pillar Projects Measure M Baseline Schedules

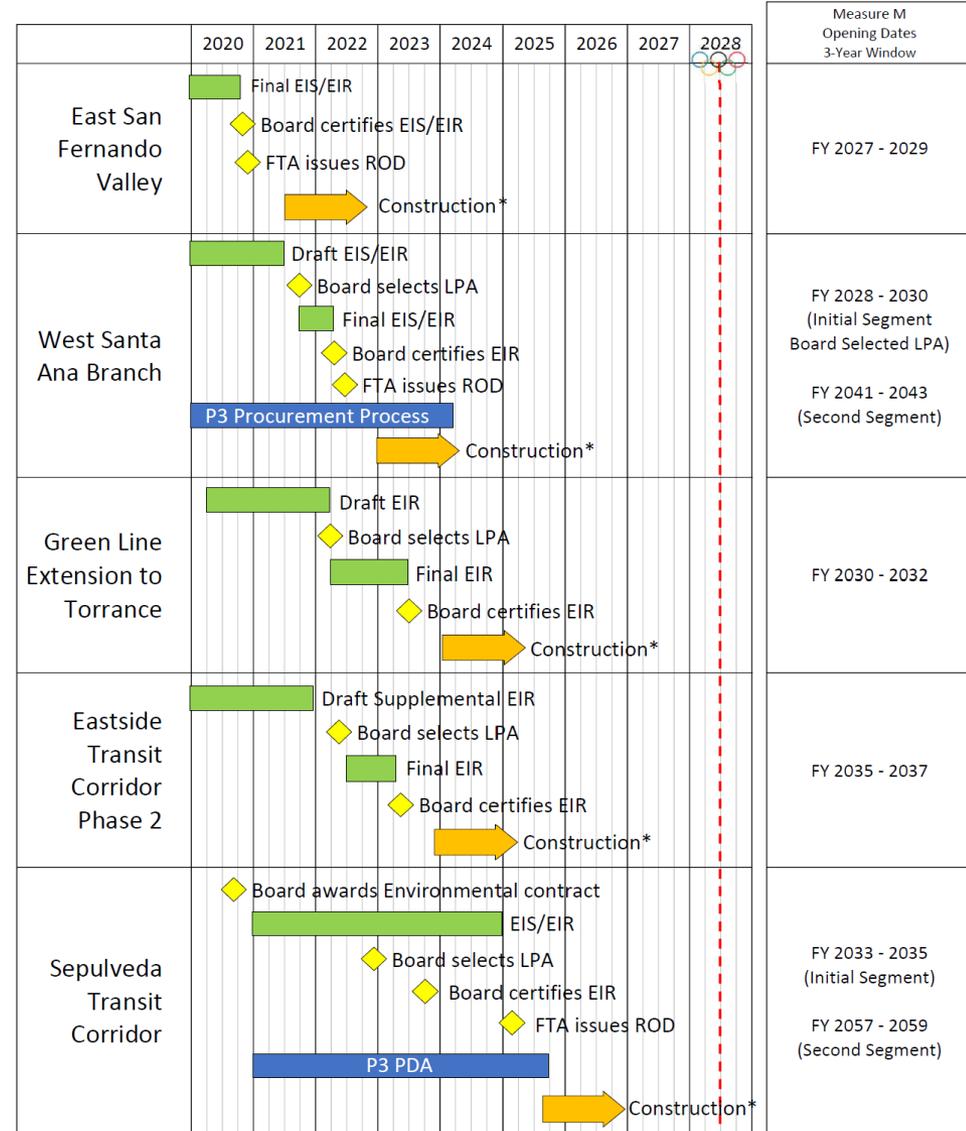

* Construction is inclusive of advanced utility relocation and right-of-way Schedules are subject to change based on funding and environmental review

West Santa Ana Branch Transit Corridor

> Status

- Draft EIS/EIR

- Anticipated Draft Release: July 2021
- Anticipated LPA Selection: Fall 2021

> Key Activities in April

- Submitting third Administrative Draft to FTA on June 9, 2021
- UPRR ongoing coordination on commercial development study
- 15% design work continues to conduct field surveys of utilities
- 3rd Party Coordination with Caltrans and Army Corps
- Preparing for public outreach and public hearings during the 45-day circulation period

> Next Actions

- Incorporate 3rd round of FTA comments on the administrative draft
- Release Draft EIS/EIR in July
- July to August: Community engagement during the release of the Draft EIS/EIR



Green Line Extension to Torrance

> Status


- Draft EIR + Advanced Conceptual Engineering tasks are proceeding (15% design)

> Key Activities

- Review of over 700 comments received during the scoping period to incorporate necessary public issues into environmental review
- Ongoing coordination meetings with BNSF on shared track segments
- Engineering analysis of Hawthorne versus ROW technical issues

> Next Actions

- Ongoing outreach:
 - Cities, BNSF, Caltrans
 - Communities
- Summer Walking Tours with Community Stakeholders, Residents

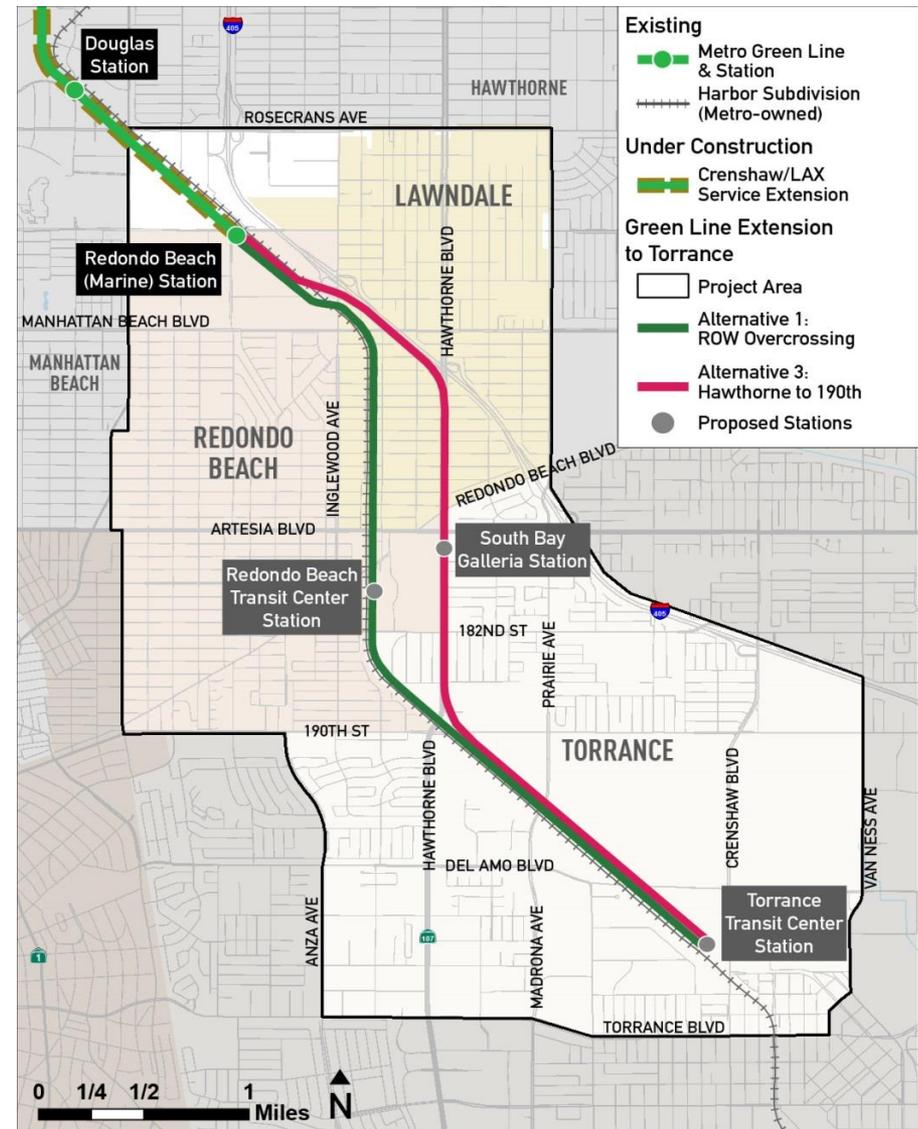

Sepulveda Transit Corridor

> Status

- Identified the five Valley-Westside alternatives entering into the environmental process
- Conduct a virtual community meeting on June 8, 2021, updating the community of project activities since the publication of the Feasibility Study and provide an overview of the upcoming environmental process

> Key Activities

- Preparing Notice to Proceed (NTP) for Pre-Development Agreement (PDA) teams
- Preparing for virtual community meeting on June 8, 2021

> Next Actions

- Preparation for Environmental Scoping Period in Fall 2021



NoHo to Pasadena BRT

> Status

- Following Board approval of Proposed Project in May, Project is now in FEIR phase

> Key Activities

- Ongoing stakeholder outreach to inform Project design
 - March 2021 – Conducted 3 meetings with Eagle Rock stakeholders and businesses (80 participants)
 - April 2021 – Corridor-wide community meeting (369 total attendees) to present the recommended Proposed Project prior to Board approval in May
 - April 2021 – Staff provided response to December Board motion on optional left-side boarding
 - May 2021 – Metro Board approved the Proposed Project Preferred Alternatives

> Next Actions

- Summer 2021 – Conduct further studies in Eagle Rock and Burbank in response to Board Direction (May)
- Fall 2021 – Board certification of Final EIR



Countywide Planning Dashboard

Pillar Projects									
	Project Name	Env Completion (FY)	Measure M Opening (FY)	Project Phase				Date	Action/Status
				AA	Draft Env	Final Env	Construction		
1	West Santa Ana Branch LRT	2022	2028-2030		X			April 2021	Approve Gateway COG Funding Agreement Modification and Extension
								July 2021	Release of Draft EIS/EIR
2	Green Line Extension to Torrance LRT	2023	2030-2032		X			April 2021	Review of EIR Scoping comments
								March 2022	Receive Draft EIR and Select Locally Preferred Alternative
3	Eastside Transit Corridor Phase 2	2024	2035-2037		X			Fall 2021	Select Locally Preferred Alternative (LPA)
4	Sepulveda Transit Corridor	2025	2033-2035	X				Fall 2021	Environmental Scoping

Other Measure M Projects									
	Project Name	Env Completion (FY)	Measure M Opening (FY)	Project Phase				Date	Action/Status
				AA	Draft Env	Final Env	Construction		
5	East San Fernando Valley Transit Corridor LRT	2020	2027-2029				X	Summer 2021	Environmental Clearance completed; initiate Supplemental ROW Study.
6	North San Fernando Valley BRT	2021	2023-2025		X			Summer 2021	Approve Proposed Project
7	North Hollywood - Pasadena BRT	2022	2022-2024			X		May 2021	Received Draft EIR and initiated Final EIR
8	Crenshaw Northern Extension LRT	2023	2047-2049		X			Fall 2021	EIR Scoping period completed. Initiate Post-Scoping Alternatives Report.
9	LA River Path (central gap)	2024	2025-2028		X			January 2022	Receive Draft EIR and Select Locally Preferred Alternative
10	Vermont Transit Corridor	2024	2028-2030	X				May 2021	Award Environmental Contract

Non-Measure M Projects				Project Phase				Date	Action/Status
	Project Name	Env Completion (FY)	Opening/ Completion (FY)	AA	Draft Env	Final Env	Construction		
11	Centinela Grade Separation	2021	2025			X		Summer 2021	Approve funding and project delivery plan
12	LAUS Forecourt and Esplanade Improvements	2021	2023			X		June 2022	Life of Project Approval
13	Rio Hondo Confluence Station Feasibility Study	TBD. Feasibility Study anticipated to be completed in 2022	TBD	X				TBD	Receive Feasibility Study Report and determine next steps for the potential Rio Hondo Confluence Station
14	Rail-to-River ATC (Segment B)	TBD. Supplemental study	TBD	X				Fall 2021	Receive Supplemental Alternatives Analysis Select Revised Locally Preferred Alternative
15	Arts District/ 6th Street Station HRT	TBD	TBD		X			April 2021	Initiate EIR Scoping
16	First/Last Mile Implementation in Transit Corridor Projects (PLE 2 and forward)	varies by project	varies by project					Summer 2021	Approve FLM Plan for PLE 1; Other periodic project-specific actions in the future;

Strategies/ Policies				Phase		Date	Action/Status
	Project Name	Groundbreaking / Initiation (FY)	Opening/ Completion (FY)	Policies/ Strategic Plans	Implementation Plans		
17	Transit Oriented Communities (TOC) Implementation Plan:Semi-Annual Reports	Ongoing	Ongoing		X	Summer 2021	Report on TOC Implementation Plan Semi Annual Reports
18	BRT Vision and Principles Study	2019	2021	X		June 2021	Response to March 2021 Board Motion
19	First/Last Mile Guidelines	N/A	N/A	X		May/June 2021	Adopt Guidelines
20	Joint Development Policy	N/A	N/A	X		May 2021	Joint Development Policy Paper published and presented at January Board Adopt Revisions to Policy
