

Metro Center Project



Bryan Pennington
Chief Program Management Officer

Recommendation



The report seeks authority to replace lapsed Proposition 1B California Transit Security Grant Program funds up to a maximum of \$32.2 million with Proposition C 5% Security funds for the Metro Center Project and commits to a report back with the findings of the special review by Management Audit Services (MAS)

Project Funding

- **Original Grant Award 2011**
- **Subsequent Grant Extensions Provided by the State**
- **Funding has Partially Lapsed**
- **Proposed Fund Replenishment to Complete Project**

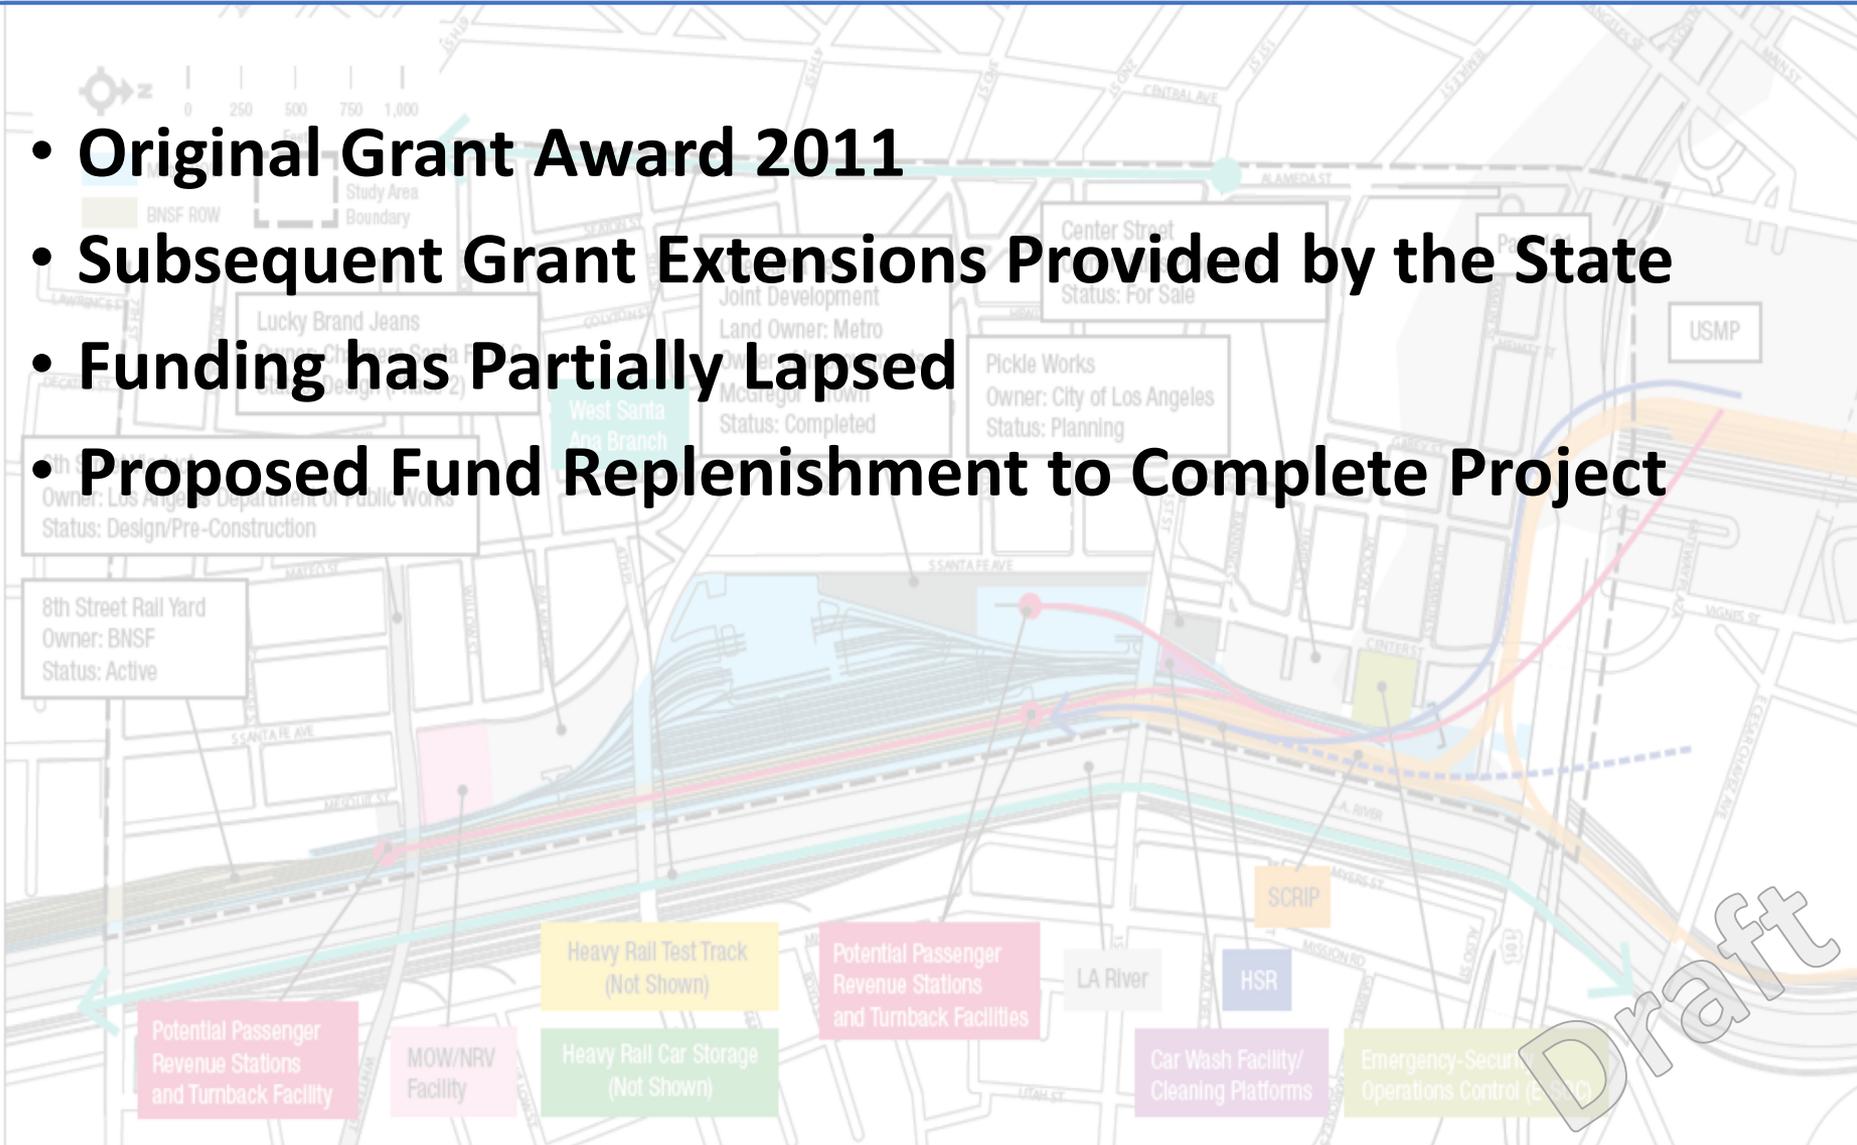


Exhibit 2: All Projects Map

Status of the Project

- Expenditures to Date – \$86.3 million
- Completion Status – Project 70% complete
- Projected Completion 2023



Next Steps

- **Provide Replacement Funding Timely**
- **Special Review Report Back**
- **Complete Project to meet Prop 1B commitments**

