ATTACHMENT A

Subway Cellular Project

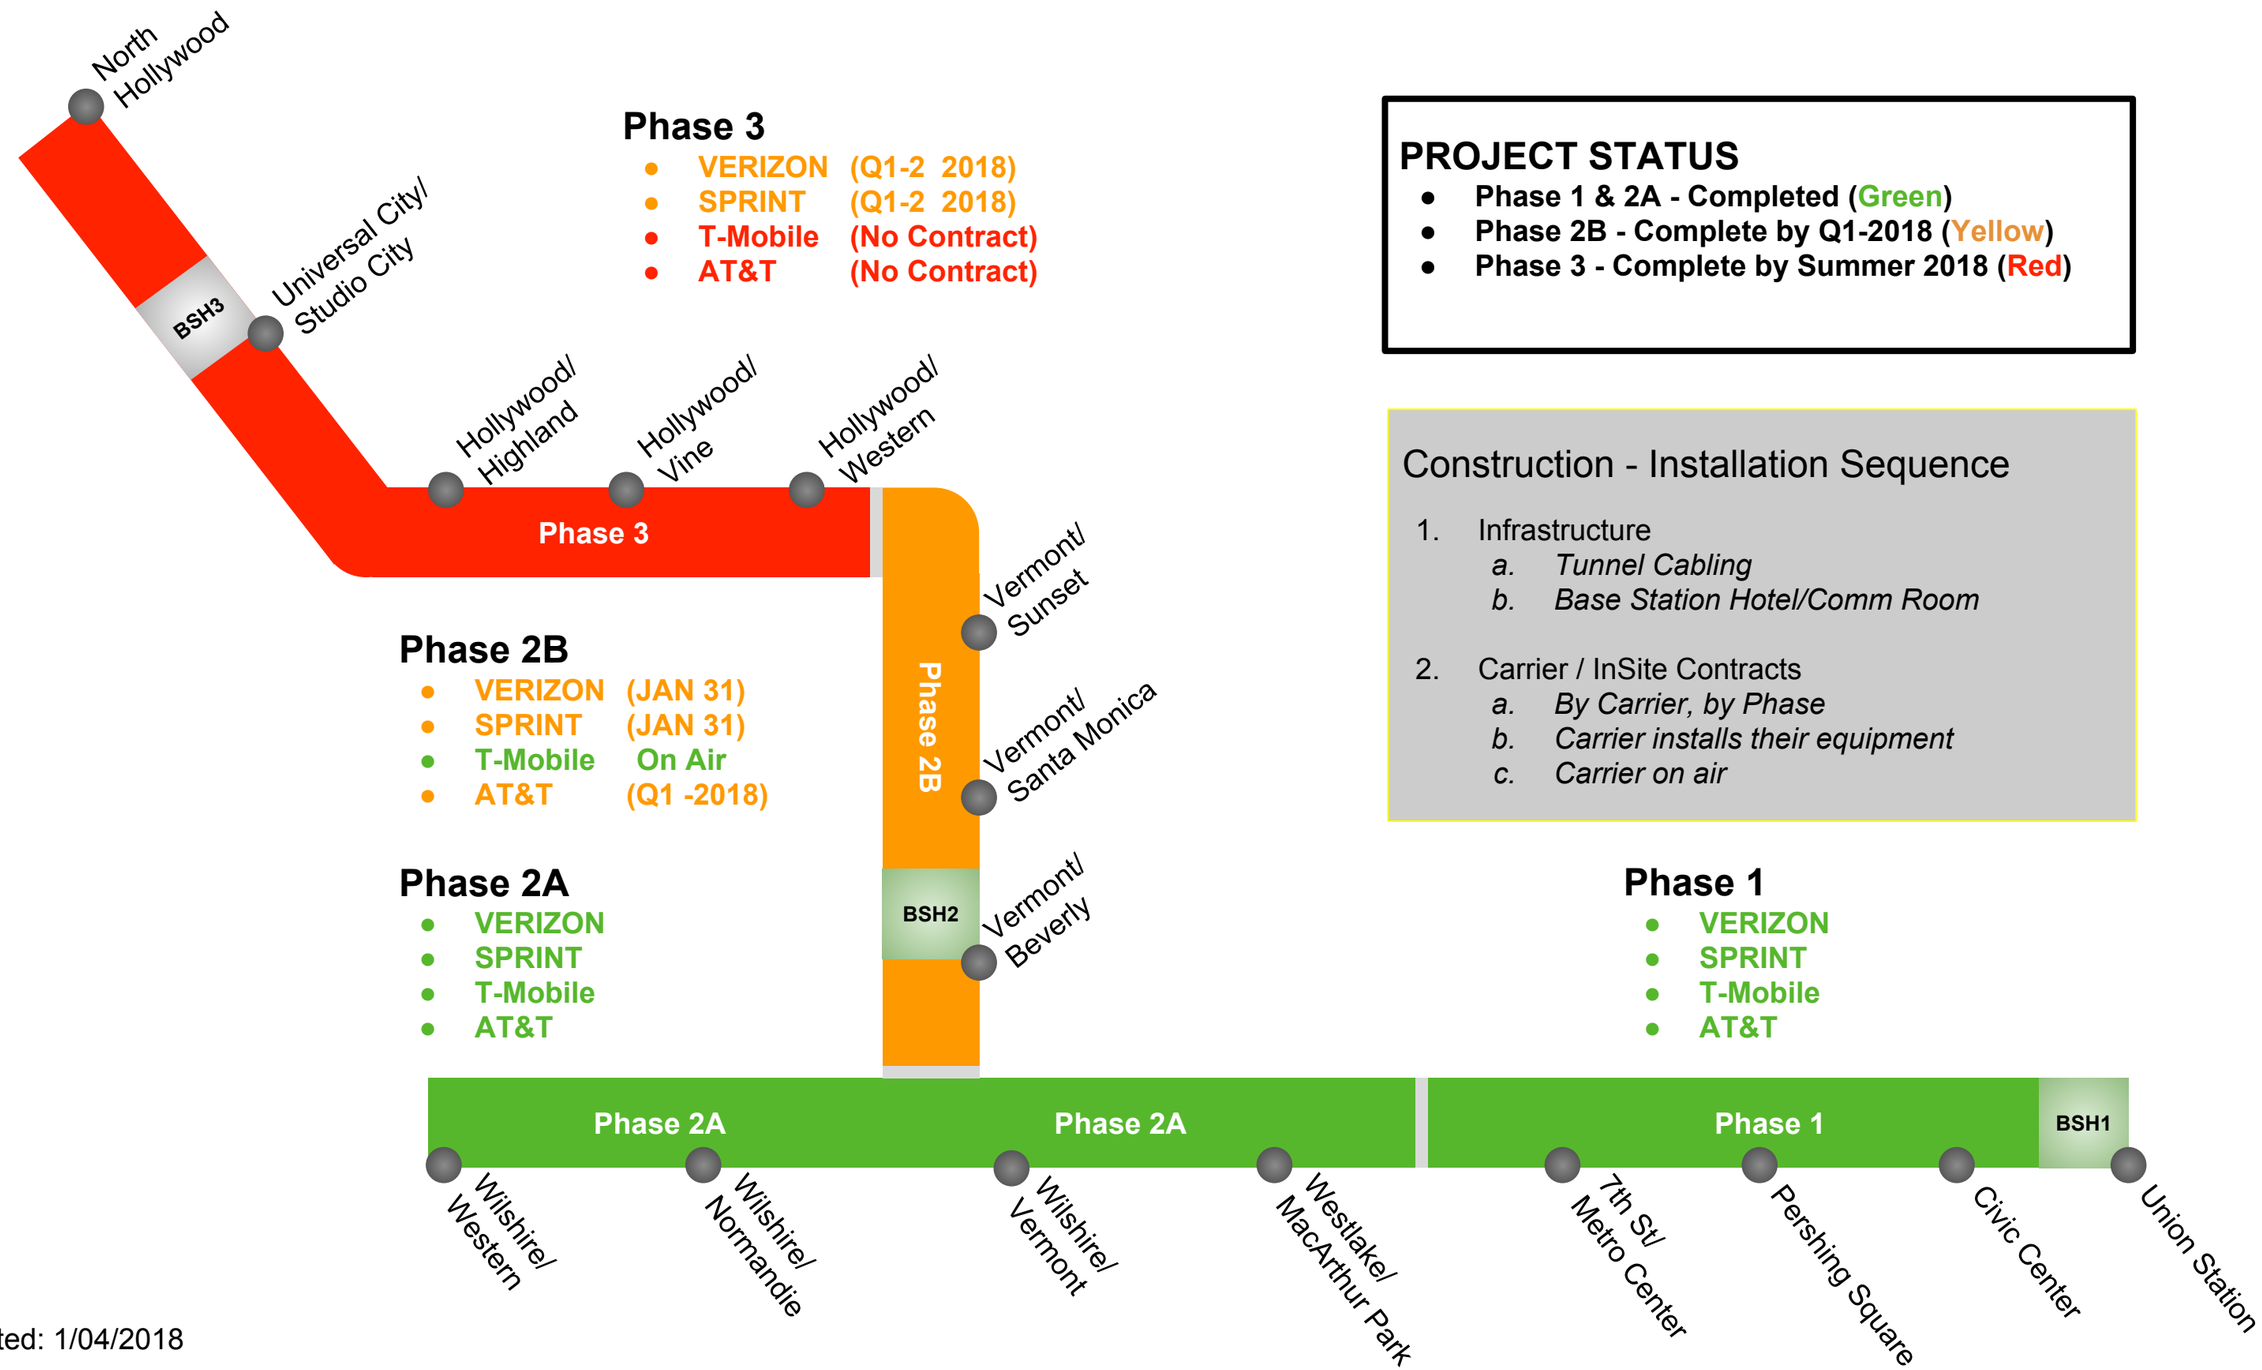

Phase 3

- VERIZON (Q1-2 2018)
- SPRINT (Q1-2 2018)
- T-Mobile (No Contract)
- AT&T (No Contract)

Phase 2B

- VERIZON (JAN 31)
- SPRINT (JAN 31)
- T-Mobile On Air
- AT&T (Q1 -2018)

Phase 2A

- VERIZON
- SPRINT
- T-Mobile
- AT&T

Phase 1

- VERIZON
- SPRINT
- T-Mobile
- AT&T

PROJECT STATUS

- **Phase 1 & 2A - Completed (Green)**
- **Phase 2B - Complete by Q1-2018 (Yellow)**
- **Phase 3 - Complete by Summer 2018 (Red)**

Construction - Installation Sequence

1. Infrastructure
   a. *Tunnel Cabling*
   b. *Base Station Hotel/Comm Room*
2. Carrier / InSite Contracts
   a. *By Carrier, by Phase*
   b. *Carrier installs their equipment*
   c. *Carrier on air*

Updated: 1/04/2018
