Twenty-Eight x 2028
Status Report and Proposed Revisions

Metro

March 20, 2024

Background / Issue

- Original list approved in January 2018 included:
  - Measure R, Measure M, and other projects already slated for completion by 2028 and;
  - Aspirational projects (i.e., with accelerated schedules)

- Recommendation to replace projects that are not able to meet 2028 with projects that:
  - Align with 2028 Mobility Concept Plan
  - Can be completed before the 2028 Games
  - Fulfill Board Direction that projects correct past inequities, leave a legacy after the Games are complete, and are necessary to host a successful global event

Metro

Status Report (by numbers) – Original List of 28 Projects

- 3 projects completed
- 7 projects under construction
- 6 projects in Engineering/Final Design
- 12 projects in Planning
- 10 projects anticipated to open after 2028

Metro

Revised Twenty-Eight by `28 Project List

Project	Current Stage	Subregion (s)
1. “New Blue” Improvements to the A Line	Operations, opened 2019	GC, CC
2. Silver Line Improvement Program	Operations, opened 2020	SG, CC, SB
3. Crenshaw/LAX Line	Operations, opened 2022	CC, SB
4. Regional Connector	Operations, opened 2023	CC
5. Eastside Access Improvements	Operations, opened 2023	CC
6. Airport Metro Connector Station	Construction, target 2024	WC
7. J Line Electrification	Design, target 2024	SG, CC, SB
8. Rail to Rail, Segment A	Construction, target 2024	CC
9. North San Fernando Valley BRT	Planning, target 2025	SFV
10. Purple Line Extension, Section 1	Construction, target 2025	WC, CC
11. Gold Line Foothill Ext to Pomona	Construction, target 2025	SG
12. Purple Line Extension, Section 2	Construction, target 2025	WC
13. Rosecrans/Marquardt Grade Sep	Construction, target 2025	GC
14. New Bus Corridors	Design, target 2026	TBD
15. I-5 North Capacity Enhancements	Construction, target 2026	NC
16. Key DTLA Stations	Planning, target 2026	CC
17. NoHo to Pasadena BRT	Design, target 2027	SFV, SG
18. LA River Bike Path/Mobility Hub - SFV	Design, target 2027	SFV
19. G Line Travel Time & Safety Features	Design, target 2027	SFV
20. Purple Line Extension, Section 3	Construction, target 2027	WC
21. Mobility Hubs in SFV	Planning, target 2027	SFV
22. Gateway Cities MCP Projects	Planning, target 2027	GC
23. LRT Speed & Reliability Improvements	Planning, target 2027	CC
24. Bus Only Lanes (Olympic/Venice)	Planning, target 2027	WC
25. I-105 Express Lanes, Segment 1	Design, target 2028	SB, GC
26. SR 57/60 Interchange Improvements	Construction, target 2028	SG
27. Vermont Transit Corridor BRT	Planning, target 2028	CC
28. I-405 Integrated Corridor Management	Design, target 2028	SB

Revised Twenty-Eight x `28 Project List Map

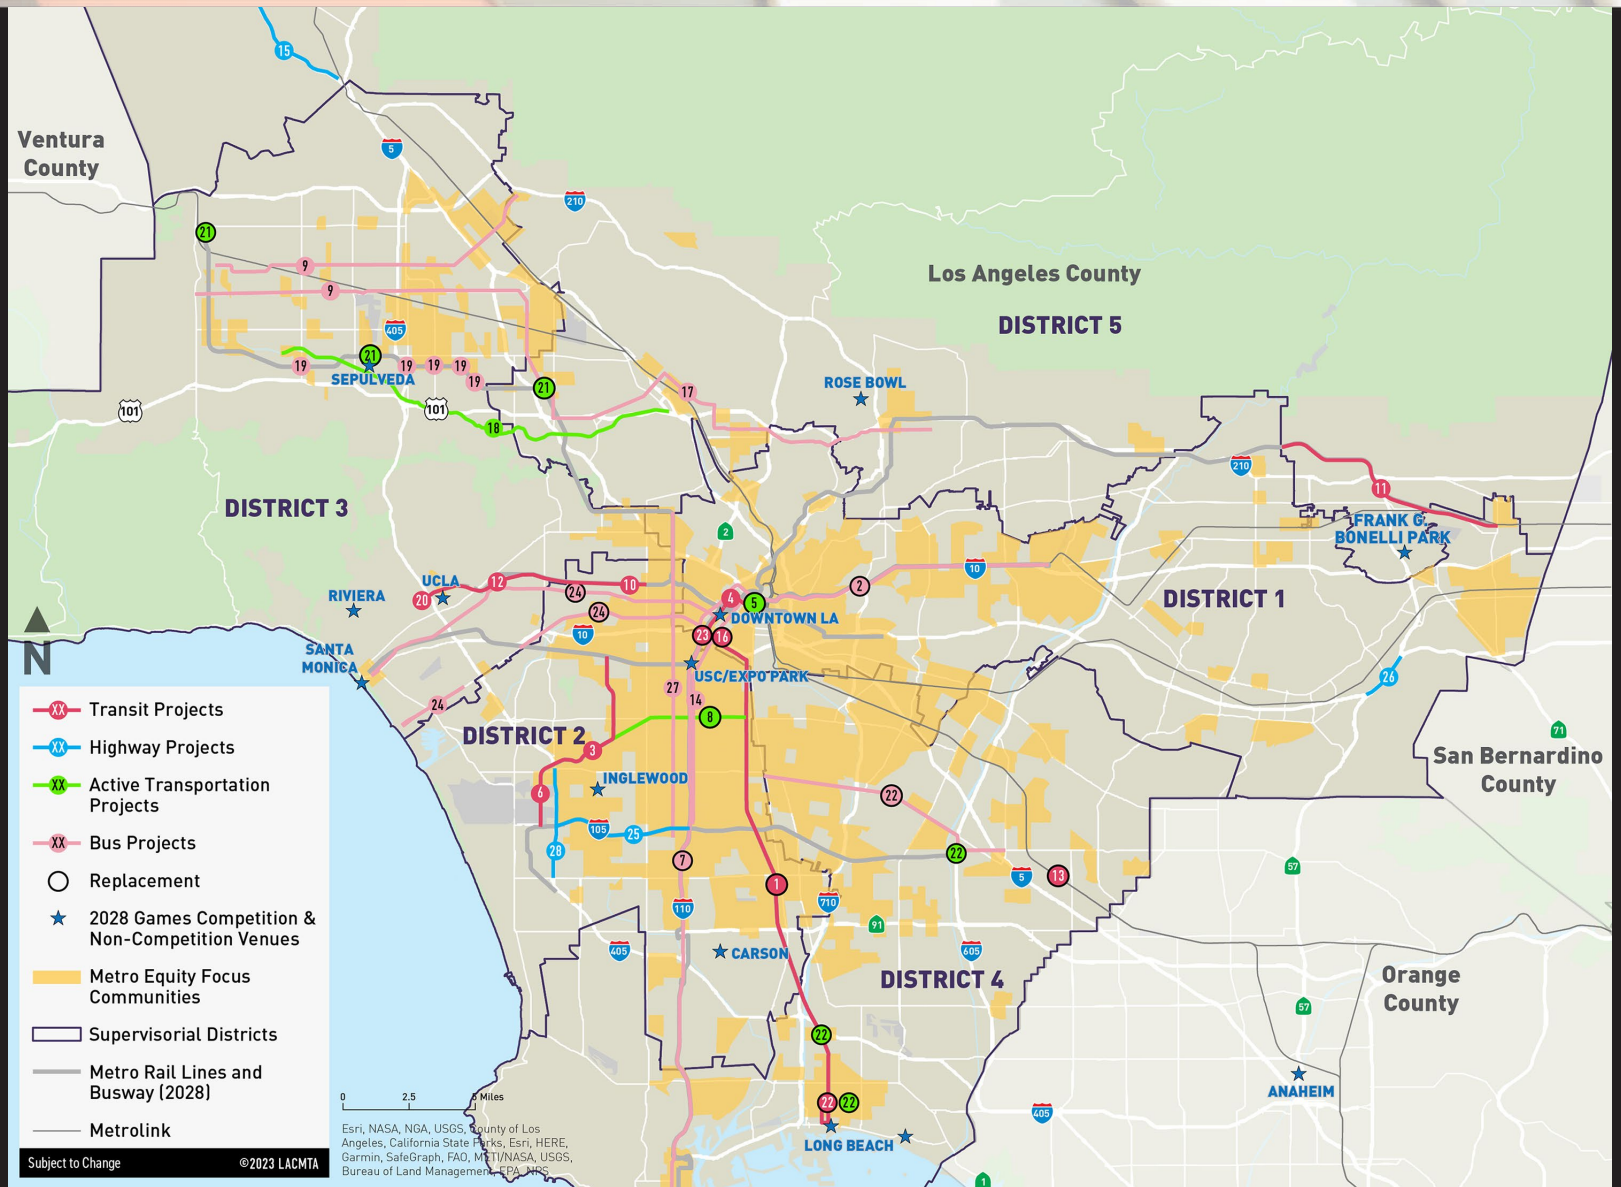

Status Report (by numbers) – Revised List of 28 Projects

- 5 projects completed
- 9 projects under construction
- 7 projects in Engineering/Final Design
- 7 projects in Planning

Metro

Additional Revisions

- Gold Line Foothill Extension 2B (to Claremont) - Revise the terminus to Pomona station to reflect current project limits. The Pomona to Montclair segment is not yet funded.

- Vermont Transit Corridor BRT - Focused on delivering the core transit travel time improvements.

- I-105 Express Lanes -Phase 1(between I-405 and I-110).

- I-405 South Bay Curve Improvements - Revise project title to clarify the scope: The Integrated Corridor Management improvements on I-405, between Manchester Ave. and Rosecrans Blvd. are underway).

Metro

Next Steps

- Continue to pursue funding for unfunded MCP projects - it remains the north star as we pursue funding collaboratively with our partners in the cities, the county, the region, and the state.
- Continue to monitor and report back on a regular basis on the status of the revised Twenty-eight by ’28 project list.

Metro
