

**Board Report 2024-0521**


**January 2025**

**Discontinue Beverly Hills North Portal  
Project**

## North Portal Project Requirements from Purple Line Section 2 Settlement Agreement

- Not to exceed total of \$78,500,000 – Split 50/50 by between Metro and City
- Metro to design and construct inside the Station Box
  - Provide infrastructure to accommodate the North Portal Project
  - Provide a new cantilevered walkway connecting concourse to North Portal Project
- Metro to support City's design and construct outside the Station Box
  - Provide design support to City
  - Provide construction coordination with both City and Metro Contractors

# DISCONTINUE BEVERLY HILLS NORTH PORTAL PROJECT

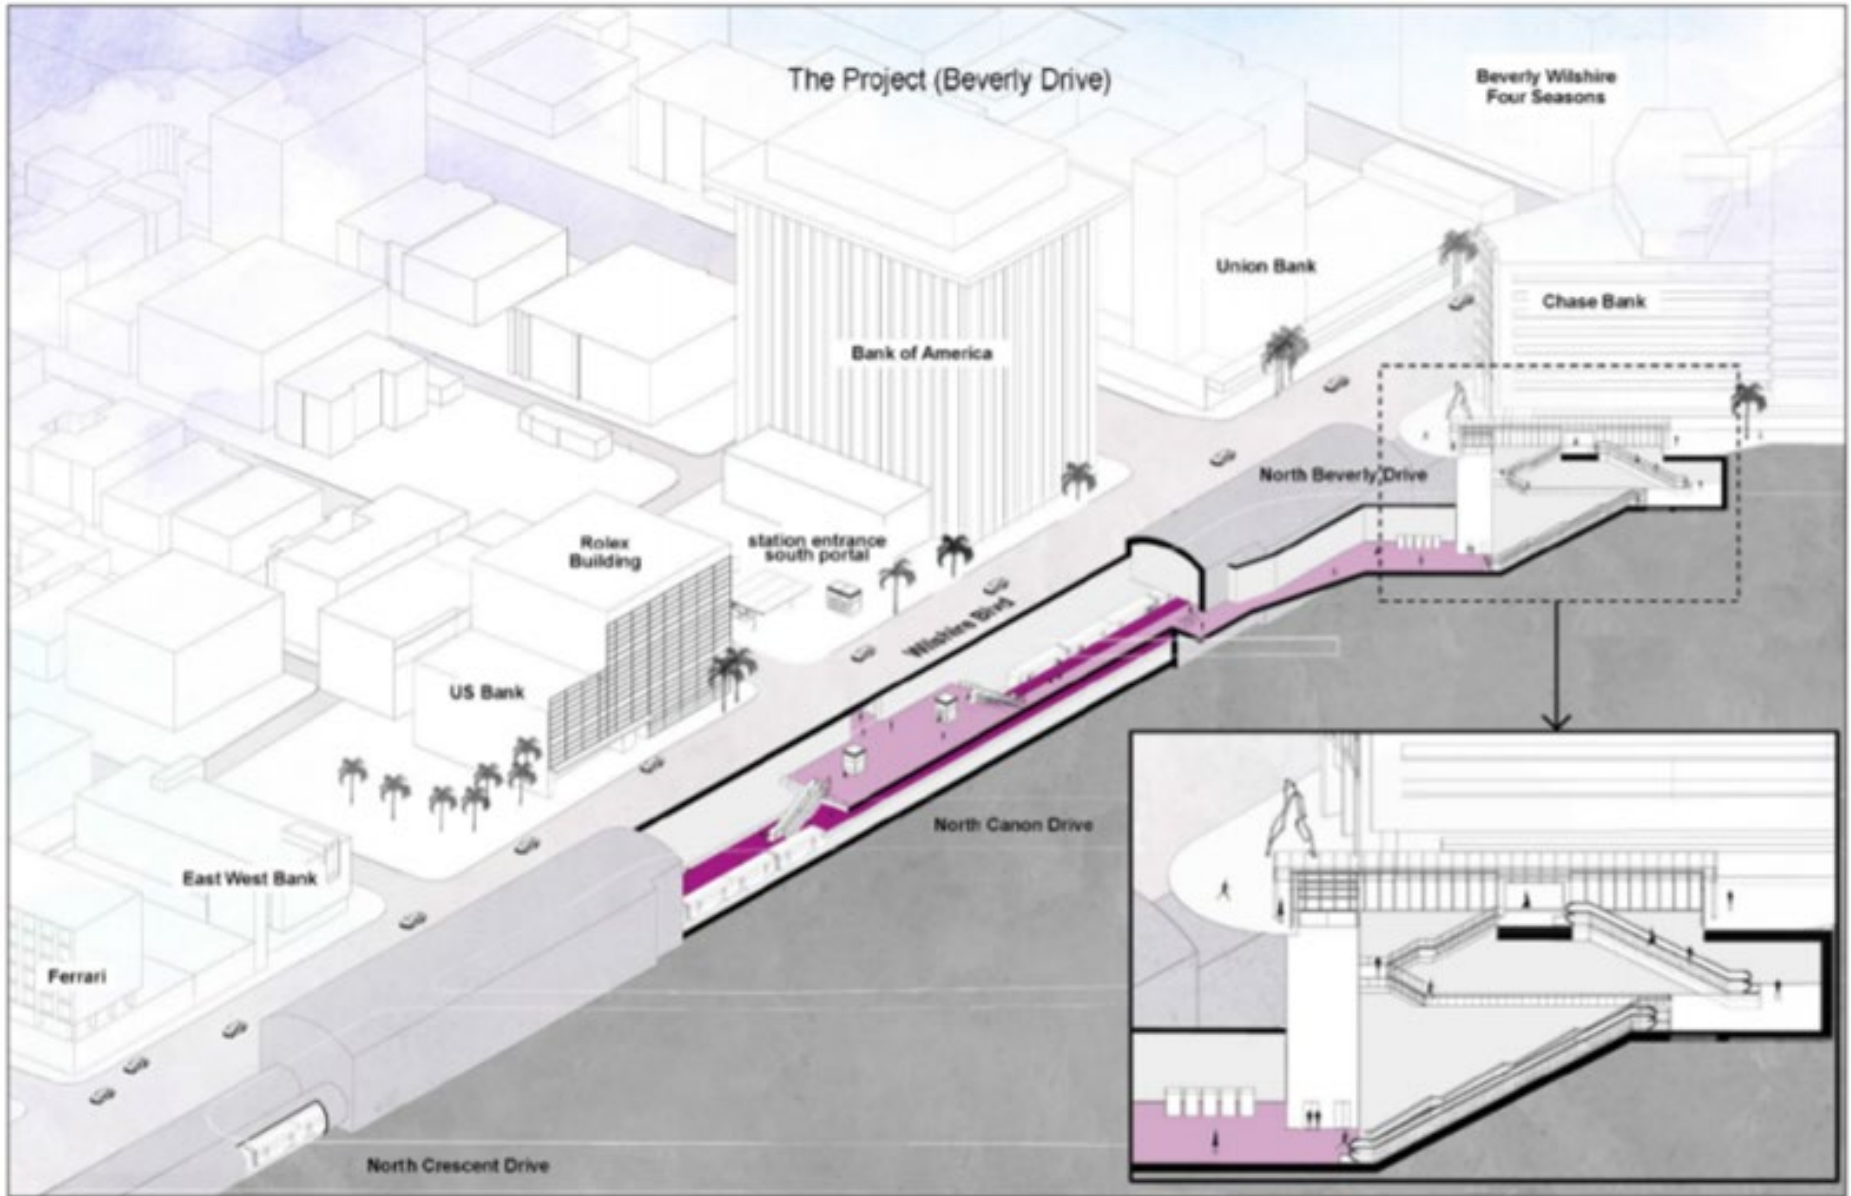

## City of Beverly Hills Recent Actions

- **March 2023**
  - HDR completes 15% design
  - HDR revises total project cost to \$134,200,000
  - Revised cost exceeds Not to Exceed Agreement of \$78,000,000
- **May 2024**
  - Beverly Hills City Council votes to discontinue the North Portal Project

## Conclusion

- Board Considerations
  - **Recommended** – Discontinue the North Portal Project
  - **Not Recommended** – Advance the North Portal Project (Requires more funding)
- Next steps for Project Staff
  - Reconcile expenses from each Party per terms of Settlement Agreement
  - Close out the Beverly Hills North Portal Project
